
Sauce & Spoon Project Plan

Project start (Monday of week 1): ene 12, 2026 *Planned launch: Apr 1, 2026*

Task	Notes	Start Date	Due Date	Duration	Task Owner	Status
Milestone: Review the project charter with Omar and get his approval	**Deanna introduces Peta**	**ene 12**	**ene 12**	**1**	**Peta**	Not Started
Milestone: Tablet vendor selected and contract signed		**ene 13**	**feb 26**	**33**	**Peta**	Not Started
Research tablet ordering system options and vendor packages, and generat	Include Terrific Tablets packages and branding	ene 13	ene 26	10	Peta	Not Started
Test out tablet systems with GMs and kitchen managers	Check real-time menu updates for Carter	ene 27	feb 2	5	Gilly / Alex	Not Started
Choose the tablet vendor and package	Depends on cost, test results and branding package	feb 3	feb 6	4	Peta	Not Started
Create the contract and statement of work with the tablet vendor	Scope, installation, branding, delivery schedule	feb 9	feb 16	6	Peta / Seydou	Not Started
Decide how many tablets are needed at each location	Needed before the order is placed	feb 9	feb 10	2	Gilly / Alex	Not Started
Order the tablets from Terrific Tablets and wait for delivery	7-10 days shipping	feb 17	feb 26	8	Seydou	Not Started
Milestone: Tablet installation complete		**feb 9**	**mar 11**	**23**	**Peta**	Not Started
Assess the installation scope at each pilot location	WiFi coverage, tables to wire, charging approach	feb 9	feb 10	2	Seydou	Not Started
Schedule the electrician to wire the tables	Book specific dates with the vendor	feb 17	feb 27	9	Seydou	Not Started
Electrician wires the tables at both locations (two half-days at each)	Restaurants cannot close for a full day	mar 2	mar 5	4	Electrician	Not Started
Select protective cases and mounts and set up a daily charging routine	Tablets must survive spills and drops	feb 17	feb 19	3	Seydou	Not Started
Replace any broken or faulty tablets	Vendor expedites replacements overnight	mar 6	mar 9	2	Seydou	Not Started
Confirm the POS version with Gilly (FlatPlate 3.0 or higher required)	Decides whether the POS update is needed	feb 9	feb 10	2	Gilly	Not Started
Update the POS system with FlatPlate if it is below version 3.0	Low confidence: never upgraded before	feb 11	feb 16	4	Gilly / FlatPlate	Not Started
Sync the tablet software with the POS	3-4 hours; low confidence	mar 6	mar 6	1	Seydou	Not Started
Test the tablet ordering process end to end after installation	Orders reach kitchen, charging, menu updates	mar 10	mar 11	2	Peta	Not Started
Milestone: Branded menu loaded on the tablets		**feb 9**	**mar 13**	**25**	**Peta**	Not Started
Get the menu items and coupon values for the tablets from Carter	Follow up with Carter; Deanna can step in	feb 9	feb 17	7	Carter	Not Started
Design the branded tablet menu mock-ups to match the printed menus	Requires the vendor branding package	feb 18	feb 24	5	Seydou / Marketing	Not Started
Load the approved menu, coupons and branding into the tablets	3-4 hours once mock-ups are approved	mar 12	mar 12	1	Seydou	Not Started
Check that digital menu items, prices and allergens match the printed menus	Recheck whenever the menu changes	mar 13	mar 13	1	Carter / Peta	Not Started
Milestone: Training complete		**feb 17**	**mar 18**	**22**	**Peta**	Not Started
Plan the trainings: draft the plan and set dates at each location	About one week of preparation	feb 17	feb 24	6	Peta / Gilly / Alex	Not Started
Hold a GM-led staff meeting at each location to get waitstaff buy-in	Buy-in first; different day than training	feb 25	feb 26	2	Gilly / Alex	Not Started
Train a small group of key staff (GMs and key waitstaff) with Seydou	Managers first, on its own day	mar 13	mar 16	2	Seydou	Not Started
Run the staff training at each location, led by the trained key staff	2 hours per training plus prep and debrief	mar 17	mar 18	2	Gilly / Alex	Not Started
Milestone: Launch day complete	**Ends with feedback after launch**	**feb 25**	**abr 3**	**28**	**Peta**	Not Started
Create a launch day plan: staffing, troubleshooting, etc.	Needed before the mock-service test	feb 25	mar 11	11	Peta	Not Started
Create table instructions and signage so guests know how to order	Include a way to ask a server for help	mar 16	mar 18	3	Peta / Marketing	Not Started
Contingency buffer (vendor, POS and training risks)	Absorbs low-confidence tasks	mar 19	mar 30	8	Peta	Not Started
Run a mock-service test with friends and family after the staff training	Simulates a full service before launch	mar 31	mar 31	1	Gilly / Alex	Not Started
Launch day: go live with the tablets at the pilot locations	**Pilot sites: North and Downtown**	**abr 1**	**abr 1**	**1**	**Peta**	Not Started
Collect staff and guest feedback after launch and act on it	Short guest survey and weekly staff huddles	abr 2	abr 3	2	Peta	Not Started




Timeline legend

- **Milestone**
- **Task**
- **Contingency buffer**
- **Launch day**

Sauce & Spoon Project Plan

Project start (Monday of week 1): ene 12, 2026 *Planned launch: Apr 1, 2026*

Task	Notes	Start Date	Due Date	Duration	Task Owner	Status
Milestone: Review the project charter with Omar and get his approval	**Deanna introduces Peta**	**ene 12**	**ene 12**	**1**	**Peta**	Not Started
Milestone: Tablet vendor selected and contract signed		**ene 13**	**feb 26**	**33**	**Peta**	Not Started
Research tablet ordering system options and vendor packages, and generat	Include Terrific Tablets packages and branding	ene 13	ene 26	10	Peta	Not Started
Test out tablet systems with GMs and kitchen managers	Check real-time menu updates for Carter	ene 27	feb 2	5	Gilly / Alex	Not Started
Choose the tablet vendor and package	Depends on cost, test results and branding package	feb 3	feb 6	4	Peta	Not Started
Create the contract and statement of work with the tablet vendor	Scope, installation, branding, delivery schedule	feb 9	feb 16	6	Peta / Seydou	Not Started
Decide how many tablets are needed at each location	Needed before the order is placed	feb 9	feb 10	2	Gilly / Alex	Not Started
Order the tablets from Terrific Tablets and wait for delivery	7-10 days shipping	feb 17	feb 26	8	Seydou	Not Started
Milestone: Tablet installation complete		**feb 9**	**mar 11**	**23**	**Peta**	Not Started
Assess the installation scope at each pilot location	WiFi coverage, tables to wire, charging approach	feb 9	feb 10	2	Seydou	Not Started
Schedule the electrician to wire the tables	Book specific dates with the vendor	feb 17	feb 27	9	Seydou	Not Started
Electrician wires the tables at both locations (two half-days at each)	Restaurants cannot close for a full day	mar 2	mar 5	4	Electrician	Not Started
Select protective cases and mounts and set up a daily charging routine	Tablets must survive spills and drops	feb 17	feb 19	3	Seydou	Not Started
Replace any broken or faulty tablets	Vendor expedites replacements overnight	mar 6	mar 9	2	Seydou	Not Started
Confirm the POS version with Gilly (FlatPlate 3.0 or higher required)	Decides whether the POS update is needed	feb 9	feb 10	2	Gilly	Not Started
Update the POS system with FlatPlate if it is below version 3.0	Low confidence: never upgraded before	feb 11	feb 16	4	Gilly / FlatPlate	Not Started
Sync the tablet software with the POS	3-4 hours; low confidence	mar 6	mar 6	1	Seydou	Not Started
Test the tablet ordering process end to end after installation	Orders reach kitchen, charging, menu updates	mar 10	mar 11	2	Peta	Not Started
Milestone: Branded menu loaded on the tablets		**feb 9**	**mar 13**	**25**	**Peta**	Not Started
Get the menu items and coupon values for the tablets from Carter	Follow up with Carter; Deanna can step in	feb 9	feb 17	7	Carter	Not Started
Design the branded tablet menu mock-ups to match the printed menus	Requires the vendor branding package	feb 18	feb 24	5	Seydou / Marketing	Not Started
Load the approved menu, coupons and branding into the tablets	3-4 hours once mock-ups are approved	mar 12	mar 12	1	Seydou	Not Started
Check that digital menu items, prices and allergens match the printed menus	Recheck whenever the menu changes	mar 13	mar 13	1	Carter / Peta	Not Started
Milestone: Training complete		**feb 17**	**mar 18**	**22**	**Peta**	Not Started
Plan the trainings: draft the plan and set dates at each location	About one week of preparation	feb 17	feb 24	6	Peta / Gilly / Alex	Not Started
Hold a GM-led staff meeting at each location to get waitstaff buy-in	Buy-in first; different day than training	feb 25	feb 26	2	Gilly / Alex	Not Started
Train a small group of key staff (GMs and key waitstaff) with Seydou	Managers first, on its own day	mar 13	mar 16	2	Seydou	Not Started
Run the staff training at each location, led by the trained key staff	2 hours per training plus prep and debrief	mar 17	mar 18	2	Gilly / Alex	Not Started
Milestone: Launch day complete	**Ends with feedback after launch**	**feb 25**	**abr 3**	**28**	**Peta**	Not Started
Create a launch day plan: staffing, troubleshooting, etc.	Needed before the mock-service test	feb 25	mar 11	11	Peta	Not Started
Create table instructions and signage so guests know how to order	Include a way to ask a server for help	mar 16	mar 18	3	Peta / Marketing	Not Started
Contingency buffer (vendor, POS and training risks)	Absorbs low-confidence tasks	mar 19	mar 30	8	Peta	Not Started
Run a mock-service test with friends and family after the staff training	Simulates a full service before launch	mar 31	mar 31	1	Gilly / Alex	Not Started
Launch day: go live with the tablets at the pilot locations	**Pilot sites: North and Downtown**	**abr 1**	**abr 1**	**1**	**Peta**	Not Started
Collect staff and guest feedback after launch and act on it	Short guest survey and weekly staff huddles	abr 2	abr 3	2	Peta	Not Started

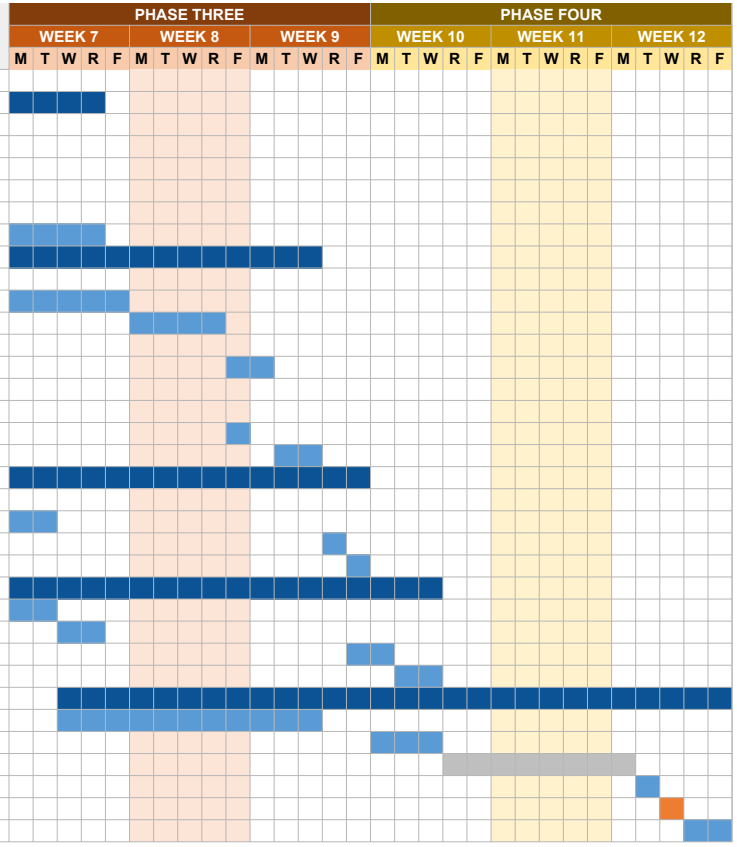

Timeline legend

- **Milestone**
- **Task**
- **Contingency buffer**
- **Launch day**
